ID		Task Name	Duration	Start	Finish
1		Start	0 days	Thu 4/1/04	Thu 4/1/04
2		Apply for Permits	28 days	Thu 4/1/04	Mon 5/10/04
3		**Site Work**	**16 days**	**Tue 5/11/04**	**Tue 6/1/04**
4		Foundation and Footing Excavation	2 days	Tue 5/11/04	Wed 5/12/04
5		Place Footings	1 day	Thu 5/13/04	Thu 5/13/04
6		Place Foundation Walls	7 days	Fri 5/14/04	Mon 5/24/04
7		Place Floor Slab	5 days	Tue 5/25/04	Mon 5/31/04
8		Conduct Foundation Inspection	1 day	Tue 6/1/04	Tue 6/1/04
9		**Framing**	**17 days**	**Wed 6/2/04**	**Thu 6/24/04**
10		Lay 1st Floor Sleepers, Sub-floor	1 day	Wed 6/2/04	Wed 6/2/04
11		Frame 1st Floor Walls	3 days	Thu 6/3/04	Mon 6/7/04
12		Install Stairs	1 day	Tue 6/8/04	Tue 6/8/04
13		Install 2nd Floor Joists	2 days	Wed 6/9/04	Thu 6/10/04
14		Frame 2nd Floor Decking	2 days	Fri 6/11/04	Mon 6/14/04
15		Frame 2nd Floor Walls	2 days	Tue 6/15/04	Wed 6/16/04
16		Frame Roof	5 days	Thu 6/17/04	Wed 6/23/04
17		Conduct Framing Inspection	1 day	Thu 6/24/04	Thu 6/24/04
18		**Sheathing**	**7 days**	**Fri 6/25/04**	**Mon 7/5/04**
19		Install 1st Floor Sheathing	3 days	Fri 6/25/04	Tue 6/29/04
20		Install 2nd Floor Sheathing	2 days	Fri 6/25/04	Mon 6/28/04
21		Install Roof Sheathing	4 days	Fri 6/25/04	Wed 6/30/04
22		Install Asphalt Shingle Roofing System	3 days	Thu 7/1/04	Mon 7/5/04
23		**Windows and Doors**	**2 days**	**Fri 6/25/04**	**Mon 6/28/04**
24		Hang Exterior Doors	1 day	Fri 6/25/04	Fri 6/25/04
25		Install Windows	2 days	Fri 6/25/04	Mon 6/28/04
26		**Exterior Finishes**	**4 days**	**Tue 6/29/04**	**Fri 7/2/04**
27		Lay Stone Masonry Wall System	4 days	Tue 6/29/04	Fri 7/2/04
28		Install Exterior Stucco Wall System	3 days	Tue 6/29/04	Thu 7/1/04
29		**Services**	**3 days**	**Tue 6/29/04**	**Thu 7/1/04**
30		Rough-in plumbing	1 day	Tue 6/29/04	Tue 6/29/04
31		Conduct Rough-in Plumbing Ispection	1 day	Wed 6/30/04	Wed 6/30/04
32		Rough-in Electrical	2 days	Tue 6/29/04	Wed 6/30/04
33		Conduct Rough-in Electrical Inspection	1 day	Thu 7/1/04	Thu 7/1/04
34		Rough-in Communications	1 day	Tue 6/29/04	Tue 6/29/04
35		**Interior Finishes**	**14 days**	**Tue 6/29/04**	**Fri 7/16/04**
36		Place Insulation	2 days	Tue 6/29/04	Wed 6/30/04
37		Conduct Insulation Inspection	1 day	Thu 7/1/04	Thu 7/1/04
38		Install Vapour Barrier and Drywall	3 days	Fri 7/2/04	Tue 7/6/04
39		Install Cabinets and Counters	2 days	Wed 7/7/04	Thu 7/8/04
40		Hang Interior Doors	2 days	Wed 7/7/04	Thu 7/8/04
41		Finish Plumbing	2 days	Thu 7/1/04	Fri 7/2/04
42		Conduct Finish Plumbing Inspection	1 day	Mon 7/5/04	Mon 7/5/04
43		Install Hardwood and Ceramic Tiles	3 days	Wed 7/7/04	Fri 7/9/04
44		Install Millwork	2 days	Mon 7/12/04	Tue 7/13/04
45		Install Appliances	1 day	Wed 7/14/04	Wed 7/14/04
46		Landscaping and Grounds Work	2 days	Fri 7/2/04	Mon 7/5/04
47		Install Gravel Driveway and Interlock Walkway	2 days	Fri 7/2/04	Mon 7/5/04
48		Complete final inspection for certificate of occupanc	1 day	Wed 7/14/04	Wed 7/14/04
49		Cleanup for occupancy	1 day	Thu 7/15/04	Thu 7/15/04
50		Perform final walk-through inspection	1 day	Fri 7/16/04	Fri 7/16/04

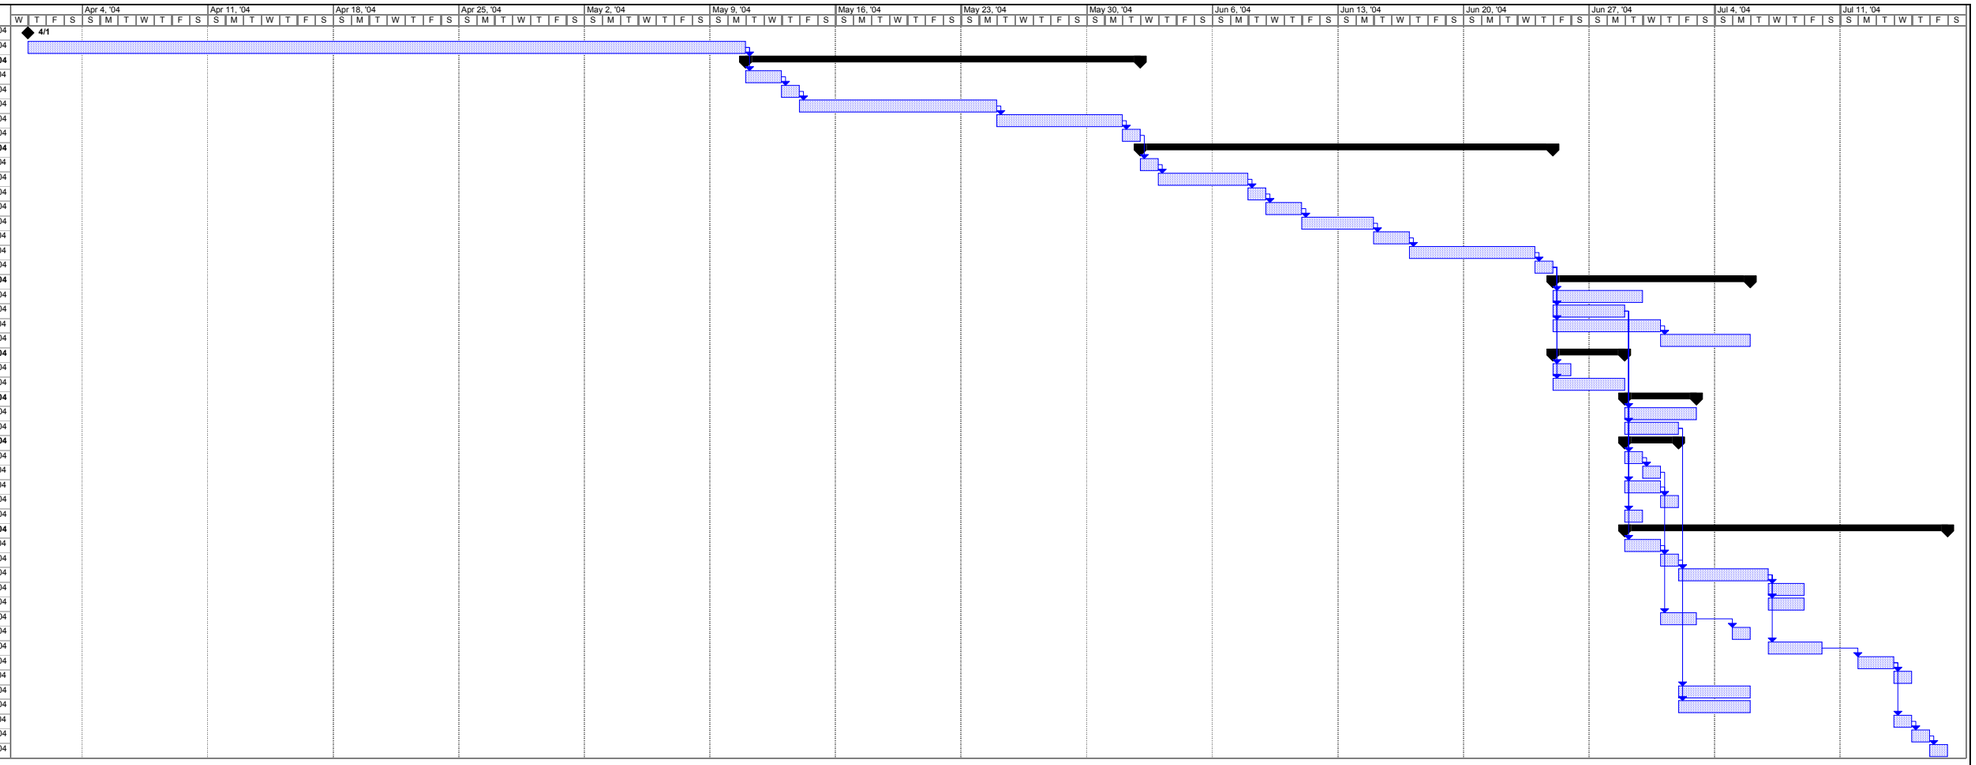

Project: CPM
Date: Tue 12/16/03

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
